Project Proposal: ERP & Digital Transformation (6 Months)

Oct 15, 2026 · Tayyaba

1. Executive Summary

NexaBridge Consulting proposes to move Al-Hamra Distribution (Pvt.) Ltd. from Excel sheets and paper registers to one ERP system in 26 weeks, for PKR 4,395,000 plus applicable taxes.

Prepared for: Management, Al-Hamra Distribution (Pvt.) Ltd., Lahore

Prepared by: NexaBridge Consulting

Today, sales, stock, purchase and accounts data sit in separate files. This causes late reports, entry mistakes and stock that is hard to track. We will bring all of it into one system, train your team, and stay with you until the system runs smoothly.

Item	Detail
Project duration	26 weeks (6 months)
Start date	Monday, 2 November 2026
Go-live (system starts running)	Monday, 5 April 2027
Final handover	Friday, 30 April 2027
Users covered	25
Total investment	PKR 4,395,000 (taxes extra)

2. About NexaBridge Consulting

NexaBridge Consulting helps growing companies replace manual work with simple, reliable digital systems. We do not sell software, so our advice is always in your interest.

Our approach has four rules:

- **Listen first.** We study your real processes before we suggest any tool.
- **Keep it simple.** We choose a system your own staff can use with confidence.
- **Work in phases.** Every phase ends with a clear output and your sign-off.
- **Report regularly.** You get a weekly update and a monthly review meeting.

Our role in this project is project manager and independent advisor. We guide software selection, supervise setup, plan data migration, train your staff and manage go-live.

3. Understanding Your Needs

Your business is growing, but your tools have not grown with it. Based on our initial discussions, these are the main gaps we will fix.

Area	How it works today	Problem it causes
Sales orders	Taken on paper and WhatsApp	Missed or duplicate orders
Stock	Excel sheets updated at day end	Wrong stock figures, stock-outs, ageing stock
Purchasing	Manual follow-up with suppliers	Late orders and weak price control
Accounts	Separate files, entered by hand	Mistakes and delayed month-end closing
Reports	Compiled by hand, 3 to 4 days	Decisions made on old information

Assumptions used in this proposal: about 120 employees, 3 warehouses, around 2,500 products, around 800 retail customers and 25 system users. We will confirm these in Month 1; if they change, we will update the scope and cost in writing.

4. Project Objectives

The main objective is one connected system for sales, stock, purchasing and accounts, running reliably by 5 April 2027. We will measure success against these targets.

#	Objective	Target by end of project
1	One system for all core departments	100% of sales, stock, purchase and accounts work done in the ERP
2	Accurate stock records	Stock accuracy of 98% or better at the 3 warehouses
3	Faster reporting	Management reports in minutes instead of 3 to 4 days
4	Faster month-end closing	Closing time cut by at least 50%

#	Objective	Target by end of project
5	Confident staff	All 25 users trained and signed off

Benefits for Al-Hamra: fewer entry mistakes, better control of stock and cash, clear numbers for owners, and a system that can grow with the business.

5. Scope of Work and Deliverables

The scope covers five ERP modules, data migration, training and 4 weeks of support after go-live. Anything outside this list needs a written change request.

Included

- Study of current processes and a gap report
- Selection of the ERP software, with a comparison of 3 shortlisted options
- Setup of Sales, Inventory, Purchasing, Accounts and Reporting modules
- Migration of customer, supplier, product, stock and opening balance data
- Testing with your team before go-live
- Training for 25 users, with simple user guides
- Go-live support for 4 weeks and a formal handover

Not included

- Custom software development beyond standard configuration
- Hardware purchases such as computers, barcode scanners or servers
- Payroll and HR modules (can be added as a second phase)
- Support after 30 April 2027 (optional plan offered in Section 14)

6. SWOT Analysis

The project is well placed to succeed, provided staff adoption and data quality are managed from day one. The SWOT below looks at the ERP project itself.

Factor	Points
Strengths	Clear management support and a defined problem. Mid-size operation, so the change is manageable. Phased plan with sign-off at every stage. Independent advisor with no software sales interest.

Factor	Points
Weaknesses	Data lives in many Excel files and paper registers, so cleaning takes time. Staff are used to manual methods. Limited in-house IT support.
Opportunities	Real-time stock and sales visibility. Lower cost of errors and stock losses. Faster credit and payment follow-up. A base for later growth, such as online ordering or more warehouses.
Threats	Staff resistance to change. Poor or incomplete data at migration. Delays in decisions or approvals. Ramadan and Eid working hours (about February to March 2027) and power or internet interruptions.

Section 12 explains how we reduce each of these risks.

7. Six-Month Implementation Strategy

We will deliver the project in five phases. Each phase has a clear output, and the next phase starts only after you approve it.


Phase	Period	Main activities	Output you approve
1. Discovery (Month 1)	Weeks 1-4	Interviews with each department. Mapping of current processes. Review of reports and data.	Current-state and gap report
2. Design and Selection (Month 2)	Weeks 5-8	Design of future processes. Demos of 3 shortlisted ERP options. Final software recommendation.	Solution design and selected software
3. Setup and Data Migration (Months 3-4)	Weeks 9-16	Configure the 5 modules. Clean and load customer, supplier, product, stock and balance data.	Configured system with migrated data
4. Testing and Training (Month 5)	Weeks 17-21	Test real business cases. Fix issues. Train 25 users. Hand out user guides.	Test sign-off and trained users

Phase	Period	Main activities	Output you approve
5. Go-Live and Handover (Month 6)	Weeks 22-26	Final preparation. Go-live on 5 April 2027. Four weeks of close support. Final handover.	Live system and final acceptance

Throughout the project we run a weekly progress update, a monthly steering meeting with management, and a shared issue and decision log.

8. Timeline and Schedule

The project runs for 26 weeks, from Monday 2 November 2026 to Friday 30 April 2027. Phases follow one another without overlap.

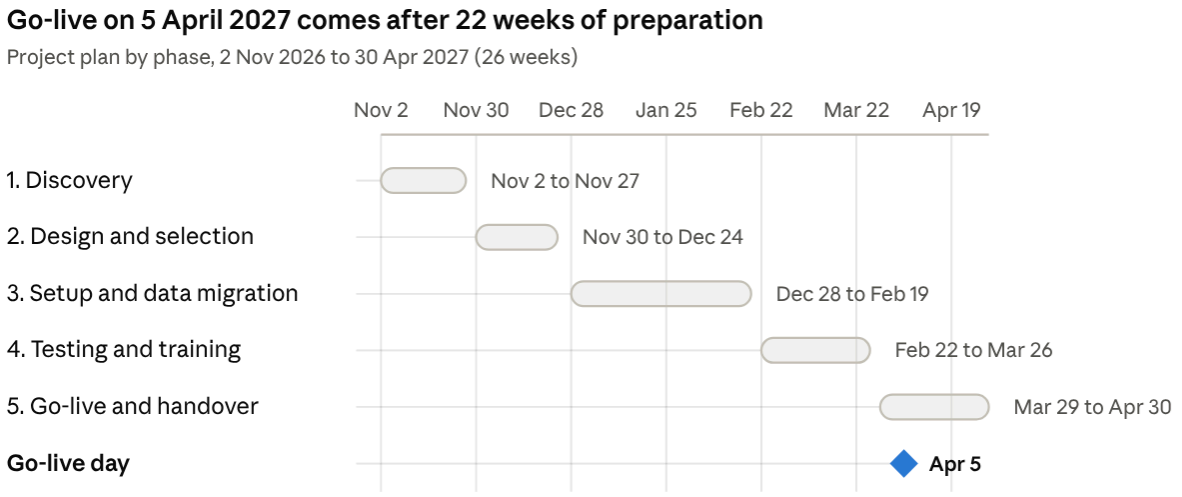

project timeline · 5 phases, go-live on 5 April 2027

The design sign-off falls on Thursday 24 December 2026 because 25 December is a public holiday. Ramadan and Eid hours (about February to March 2027) fall in Phase 4, which has time built in for this.

Milestone	Date	Linked payment
Kick-off meeting	Monday 2 November 2026	Signing payment (20%), due before kick-off
Discovery report approved	Friday 27 November 2026	None
Design sign-off and software selected	Thursday 24 December 2026	20%

Milestone	Date	Linked payment
Data migration complete	Friday 19 February 2027	30%
Testing and training signed off	Friday 26 March 2027	None
Go-live	Monday 5 April 2027	20%
Final handover and acceptance	Friday 30 April 2027	10%

9. Costing

The total project cost is PKR 4,395,000, excluding applicable taxes. All amounts are in Pakistani rupees.

Item	Basis	Amount (PKR)
Project Manager	3 months (half-time over 6 months) x PKR 300,000	900,000
ERP Functional Consultant	5 months x PKR 250,000	1,250,000
Data Migration Analyst	3 months x PKR 150,000	450,000
Trainer and Change Lead	2 months x PKR 150,000	300,000
Consulting fee subtotal		**2,900,000**
ERP licences and cloud hosting	25 users x PKR 8,000 x 6 months, billed at actual cost with no mark-up	1,200,000
Training workshops and materials	Venue, printed guides, user manuals	150,000
Project contingency	5% of consulting fee, used only with your written approval	145,000
Total project cost		**4,395,000**

How the fee is calculated: each rate is the monthly charge for one specialist, multiplied by the months that person works on your project. You pay only for the effort shown, and the software licences are passed on at our cost.

Payment schedule

Milestone	Share	Amount (PKR)
On signing the agreement	20%	879,000
Design sign-off (end of Phase 2)	20%	879,000
Data migration complete (end of Phase 3)	30%	1,318,500
Go-live	20%	879,000
Final handover and acceptance	10%	439,500
Total	**100%**	**4,395,000**

Unused contingency is deducted from the final payment. The licence figure is an estimate based on 25 users and will be confirmed once the software is selected in Phase 2.

10. Return on Investment

On our base-case assumptions, the ERP pays for itself about 13 months after the project starts, and over three years it returns PKR 12,752,000 more than it costs (a return of 123%). If the savings are only half as large, it still pays back within three years.

The full calculation, with costs, savings, assumptions and a sensitivity check, is in the separate document "Return on Investment (ROI) Analysis: ERP Project for Al-Hamra Distribution", which is part of this proposal package. We will confirm every figure against Al-Hamra's actual numbers in Phase 1.

11. Project Team and Responsibilities

Success depends on both teams. Each person below has one clear responsibility.

Team	Role	Responsibility
NexaBridge	Project Manager	Overall plan, budget, reporting and risk control
NexaBridge	ERP Functional Consultant	Process design and system configuration
NexaBridge	Data Migration Analyst	Data cleaning, loading and checking
NexaBridge	Trainer and Change Lead	User training, guides and staff support

Team	Role	Responsibility
Al-Hamra	Executive Sponsor (Owner or CEO)	Final decisions and removal of obstacles
Al-Hamra	Project Coordinator	Daily contact with NexaBridge and quick approvals
Al-Hamra	Department Heads (Sales, Warehouse, Purchasing, Finance)	Process input, testing and sign-off for their area
Al-Hamra	IT Contact	Computers, network and user access

12. Risks and How We Manage Them

We have identified six main risks. Each has an action and an owner, and we review them at every monthly steering meeting.

Risk	How we manage it
Staff resist the change	Involve staff from Month 1, train in small groups, and name a super-user in each department
Poor or incomplete data	Start data cleaning in Phase 2, run two trial migrations, and get your sign-off before loading
Delays in decisions	Agree a 3-working-day approval time and escalate to the Executive Sponsor if it is missed
Ramadan and Eid hours	Plan training around shorter working hours and keep a buffer in Phase 4
Power or internet cuts	Use a cloud-based system, and advise on backup internet and power for key sites
Scope creep	Record every new request as a written change request with its cost and time impact

13. Our Commitment to Your Satisfaction

We measure our work by your results, not by activity. You will always know where the project stands and what comes next.

- **Weekly update** every Friday: progress, issues and next steps.

- **Monthly steering meeting** with management, followed by written minutes within 24 hours.
- **Response time:** we reply to your queries within 1 working day.
- **Sign-off at every phase:** nothing moves forward without your approval.
- **Satisfaction check** at the end of each phase; we aim for a score of 4 out of 5 or better and act on any lower score.
- **Free fixes:** any error in our configuration found during the 4 weeks of go-live support is corrected at no extra charge.
- **Complete handover:** user guides, process documents and training records.

14. Terms, Assumptions and Next Steps

To keep the 2 November 2026 start, please confirm this proposal by 28 October 2026. The proposal is valid until 14 November 2026.

- Prices are in PKR and exclude applicable taxes.
- Payments follow the schedule in Section 9.
- Changes to scope, users or timeline are made only through a written change request.
- Al-Hamra will provide timely access to staff, data and premises.
- All business information shared with us is kept confidential.
- Optional support after 30 April 2027: PKR 100,000 per month, agreed separately.

Next steps

1. Review this proposal and share your questions.
2. Meet to discuss scope and costing.
3. Sign the agreement and pay the first instalment.
4. Kick-off meeting on 2 November 2026.

Acceptance

	For Al-Hamra Distribution (Pvt.) Ltd.	For NexaBridge Consulting
Name		
Title		
Signature		
Date		
